

APPLICATION ONLY

85-9205N

SEPTIC SYSTEM APPLICATION

PERMIT NO. 9205

FLATHEAD COUNTY

SANITATION OFFICE

1. TR6B SE4 NW4 ENE4 SW4 7-29-20 2. 80 Ac
Legal Description of Property Parcel Size
3. Gordon Wallis 4. None
Legal Property Owner Property Occupant
5. 149 W. Mt., Kal 560 Winfield Ln., C.F. +
Address & Phone Property Address 572 Winfield Ln
6. Proposed Dwelling: Conv. Sing. Fam. X; Mob. Home ; Dupl. ; 4-Plex ; Apart. ; Other
7. No. of Bedrooms: 2 Existing Structures: House Water: Proposed well
8. Septic System: New X Remodel Installer: Kouns

I HEREBY DECLARE the above information is true, complete and correct to the best of my knowledge. I will install the system according to the FLATHEAD COUNTY REGULATIONS FOR SEWAGE TREATMENT SYSTEMS and the terms of the permit. I acknowledge that the County has not designed my system and that these requirements do not bind or obligate the County to guarantee this system's operation. I FURTHER AGREE to call and give 24 hours ADVANCE NOTICE for REQUIRED INSPECTIONS of the SYSTEM. PLEASE PHONE 755-5300 Ext. 350!!

10/22/85 Gordon Wallis by Donna Kouns
Date Signature of Applicant

1. Septic Tank Size: 900 gallons (min.) Site Evaluator's Comments
2. Soil Type: Sand Onsite 10-24-85
How Determined: Onsite 0 to 44" fine sand
3. Depth of Water Table/Bedrock: 78 feet Only 2 possible sites -
How Determined: Previous Experience level area North of house
4. Absorption Area: 320 square feet and level area to East of
house next to road.


5. Describe Drainfield: Use 160 lineal feet of 2 foot wide trench
or 110 lineal feet of 3 foot wide trench with a
maximum depth of 36 inches. Use multiple
lines with no single line longer than 80 feet. Slope
on trench bottoms and perforated lines must be
at or near level (0 to 1%). Insure that all setback
requirements are satisfied. Insure that system
is installed in a suitable location. Insure that
all County Regulations are complied with.

10-24-85 Kenneth Hall #0570334
Date Signature Authorizing Approval of Permit Application

* These requirements establish the MINIMUM SIZE FOR THIS SEPTIC SYSTEM INSTALLATION. Permit will be voided and declared invalid if the system is not installed within 12 months of the issuance of this permit.

Please phone 755-5300 Ext. 350 for inspection when system is completely installed except for backfill. Please notify this office at least one day in advance for prompt service.

LAYOUT

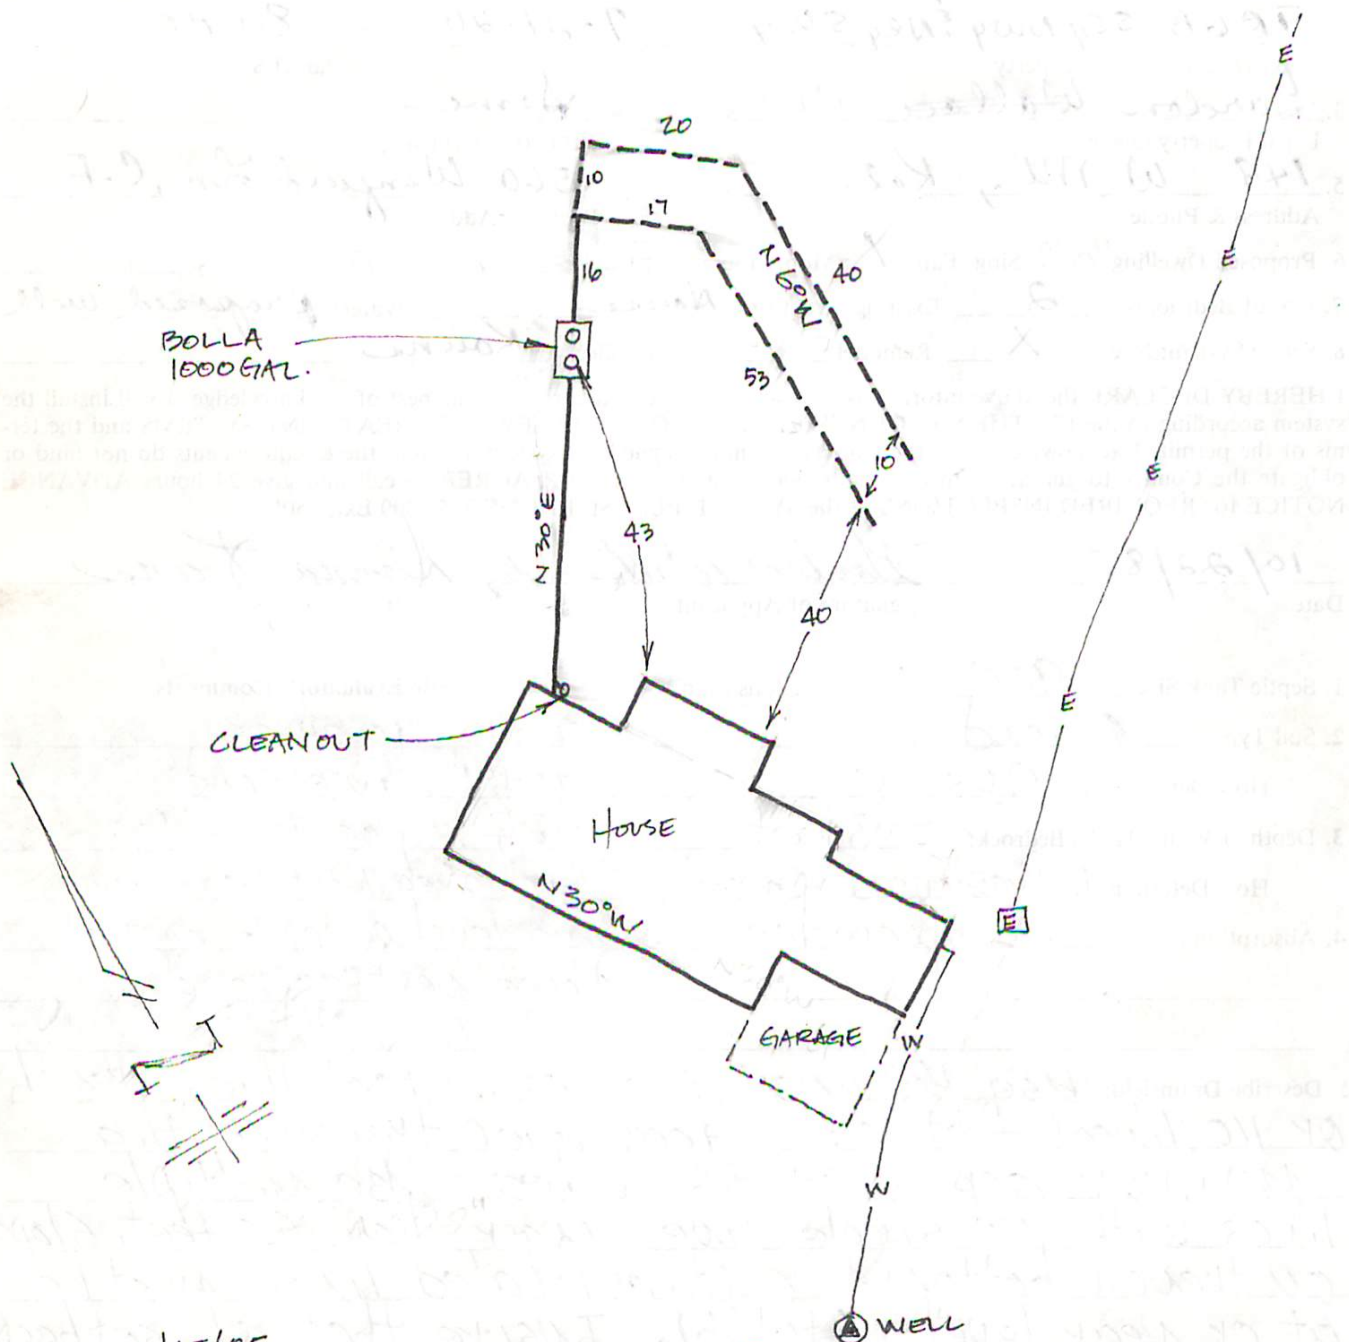

Date 11/15/85

Inspected by DREW PASLAWSKY

Approved ☒

Disapproved* ☐

Inspector Comments TRENCH DEPTH 30". 140 L.F. X 3 FT. = 420' ABSORPTION AREA. SOIL: FINE TO MEDIUM SAND.

Name of Installer: Kouma
